



ADA Curb Ramp New Construction Inspection Form (Perpendicular)

Nw 313 th ave

North-South Road Name

24952.54

Project No.

Sheet No.

Intersection No.

Nw Yorkshire st

East-West Road Name

Calibration Date

2024-10-29

(mm/dd/yy)

Ramp Style **PR**

RAMP RUN 1

Pass

Fail

Running Slope 1

8.1

≤ 8.3%

☒

>8.3%

☐

Length 1

4.9

Cross Slope 1

2.4

≤ 2.0%

☐

>2.0%

☒

Detectable Warning (Y,N)

Y

Y

☒

N

☐

Lip Height

0

1/4"

☒

>1/4"

☐

Gutter Flow Slope

N/A

2.2

≤ *

☒

>*

☐

Curb Running Slope (avg)

3.08

≤ 8.3%

☒

>8.3%

☐

Counter Slope (+/-) *2

2.8

≤ |5.0%|

☒

>|5.0%|

☐

Longest distance from corner to back of curb (see dwg on BT form)

< 5.0'

☒

≥ 5.0'

☐

Detectable warning extends full width of ramp throat opening

Y

Y

☒

N

☐

TURN SPACE ☒

LANDING ☐

NONE ☐

Pass

Fail

Width X

8.9

≥ 4.0'

☒

< 4.0'

☐

Length Y

5.0

≥ 4.0'*1

☒

< 4.0'*1

☐

Back of Ramp Obstruction (Y/N)

N

≥ 5.0'*1

☒

< 5.0'*1

☐

Slope X

2.0

≤ 2.0%

☒

>2.0%

☐

Slope Y

0.8

≤ 2.0%

☒

>2.0%

☐

MISCELLANEOUS Traversable

Pass

Fail

Flare Slope 1

☒

≤ 10%

☒

< 10%

☐

Flare Slope 2

☒

≤ 10%

☒

< 10%

☐

Clear Width (feet)

5.0

≥ 4.0'

☐

< 4.0'

☐

Intersection Control Type

SU

Slope of Road

1.6


Horizontal Gaps

≤ 1/2"

☒

> 1/2"

☐

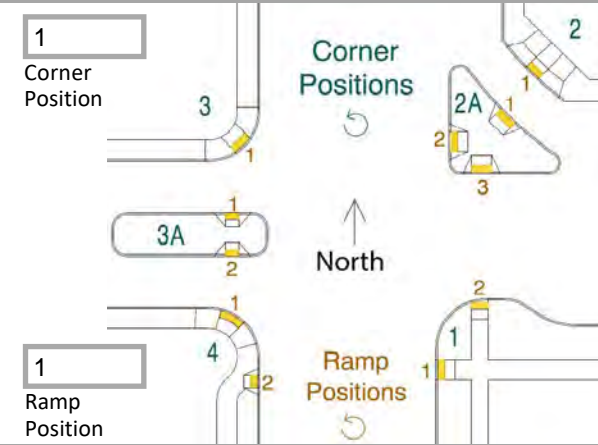

PE Stamp (required for private development)

See also Standard Drawings to assess provisions not shown: (inlets, alignment, etc.)



PERPENDICULAR RAMP (PR)

Pedestrian Access Route (to measure Clear Width)

Detectable Warning Surface

Cross Slope (2.0% max.)

Running Slope (8.3% max.)

Counter Slope (5.0% max.)

Turning Space (X & Y) (2.0% max. / 4' x 4' min.)*
* If constrained at back of walk, min. Y length is 5'.

Gutter Flow Slope (as directed)

Comments:

Crack through curb and gutter

Inspector's Signature

Date (mm/dd/yy)

Darrell Wyant

52638

Print name clearly

Certification No.

3J Consulting

Company/Agency

Reset Entire Form

Keep Intersection, Reset Fields

ADA Curb Ramp Images

Attached photos must be in .pdf format in order to be placed

