



ADA Curb Ramp New Construction Inspection Form (Perpendicular)

NW 311th Ave

North-South Road Name

24952.54

Project No.

Sheet No.

Intersection No.

NW Moon St

East-West Road Name

Calibration Date

11/6/2024

(mm/dd/yy)

Ramp Style **PR**

RAMP RUN 1

Pass

Fail

Running Slope 1

7.6

≤ 8.3%



>8.3%



Length 1

8.7

Cross Slope 1

0.8

≤ 2.0%



>2.0%



Detectable Warning (Y,N)

Y

Y



N



Lip Height

0

1/4"



>1/4"



Gutter Flow Slope

N/A

0.7

≤ *



>*



Curb Running Slope (avg)

4.8

≤ 8.3%



>8.3%



Counter Slope (+/-) *2

1.5

≤ |5.0%|



>|5.0%|



Longest distance from corner to back of curb (see dwg on BT form)

< 5.0'



≥ 5.0'



Detectable warning extends full width of ramp throat opening

Y

Y



N



TURN SPACE



LANDING



NONE



Pass

Fail

Width X

8.85

≥ 4.0'



< 4.0'



Length Y

7.75

≥ 4.0'*1



< 4.0'*1



Back of Ramp Obstruction (Y/N)

N

≥ 5.0'*1



< 5.0'*1



Slope X

2.2

≤ 2.0%



> 2.0%



Slope Y

1.2

≤ 2.0%



> 2.0%



MISCELLANEOUS Traversable

Pass

Fail

Flare Slope 1



≤ 10%



< 10%



Flare Slope 2



≤ 10%



< 10%



Clear Width (feet)

7.75

≥ 4.0'



< 4.0'



Intersection Control Type

MB

Slope of Road


1.2

Horizontal Gaps

≤ 1/2"



> 1/2"

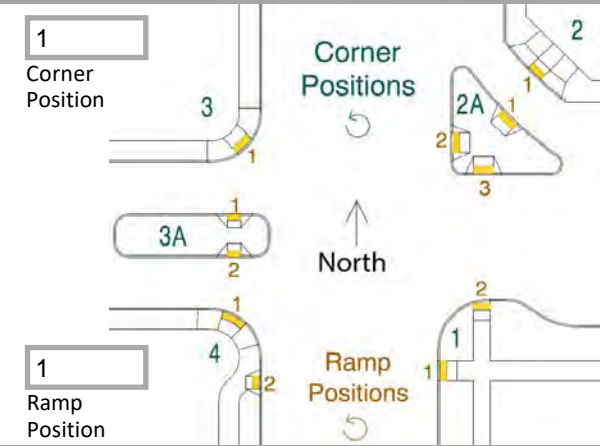

PE Stamp (required for private development)

Comments:

nan

Inspector's Signature

Date (mm/dd/yy)

Darrell Wyant

52638

Print name clearly


Certification No.

3J Consulting


Company/Agency

Reset Entire Form


Keep Intersection, Reset Fields





PERPENDICULAR RAMP (PR)


 Pedestrian Access Route (to measure Clear Width)

 Detectable Warning Surface

 Cross Slope (2.0% max.)

 Running Slope (8.3% max.)

 Counter Slope (5.0% max.)

 Turning Space (X & Y) (2.0% max. / 4' x 4' min.)*
* If constrained at back of walk, min. Y length is 5'.

 Gutter Flow Slope (as directed)

ADA Curb Ramp Images

Attached photos must be in .pdf format in order to be placed

